Colchester project Plan

smartsheet

Updated 12/15/2023
Updated 01/05/2024
updated 02/06/2024
Updated 03/08/2024

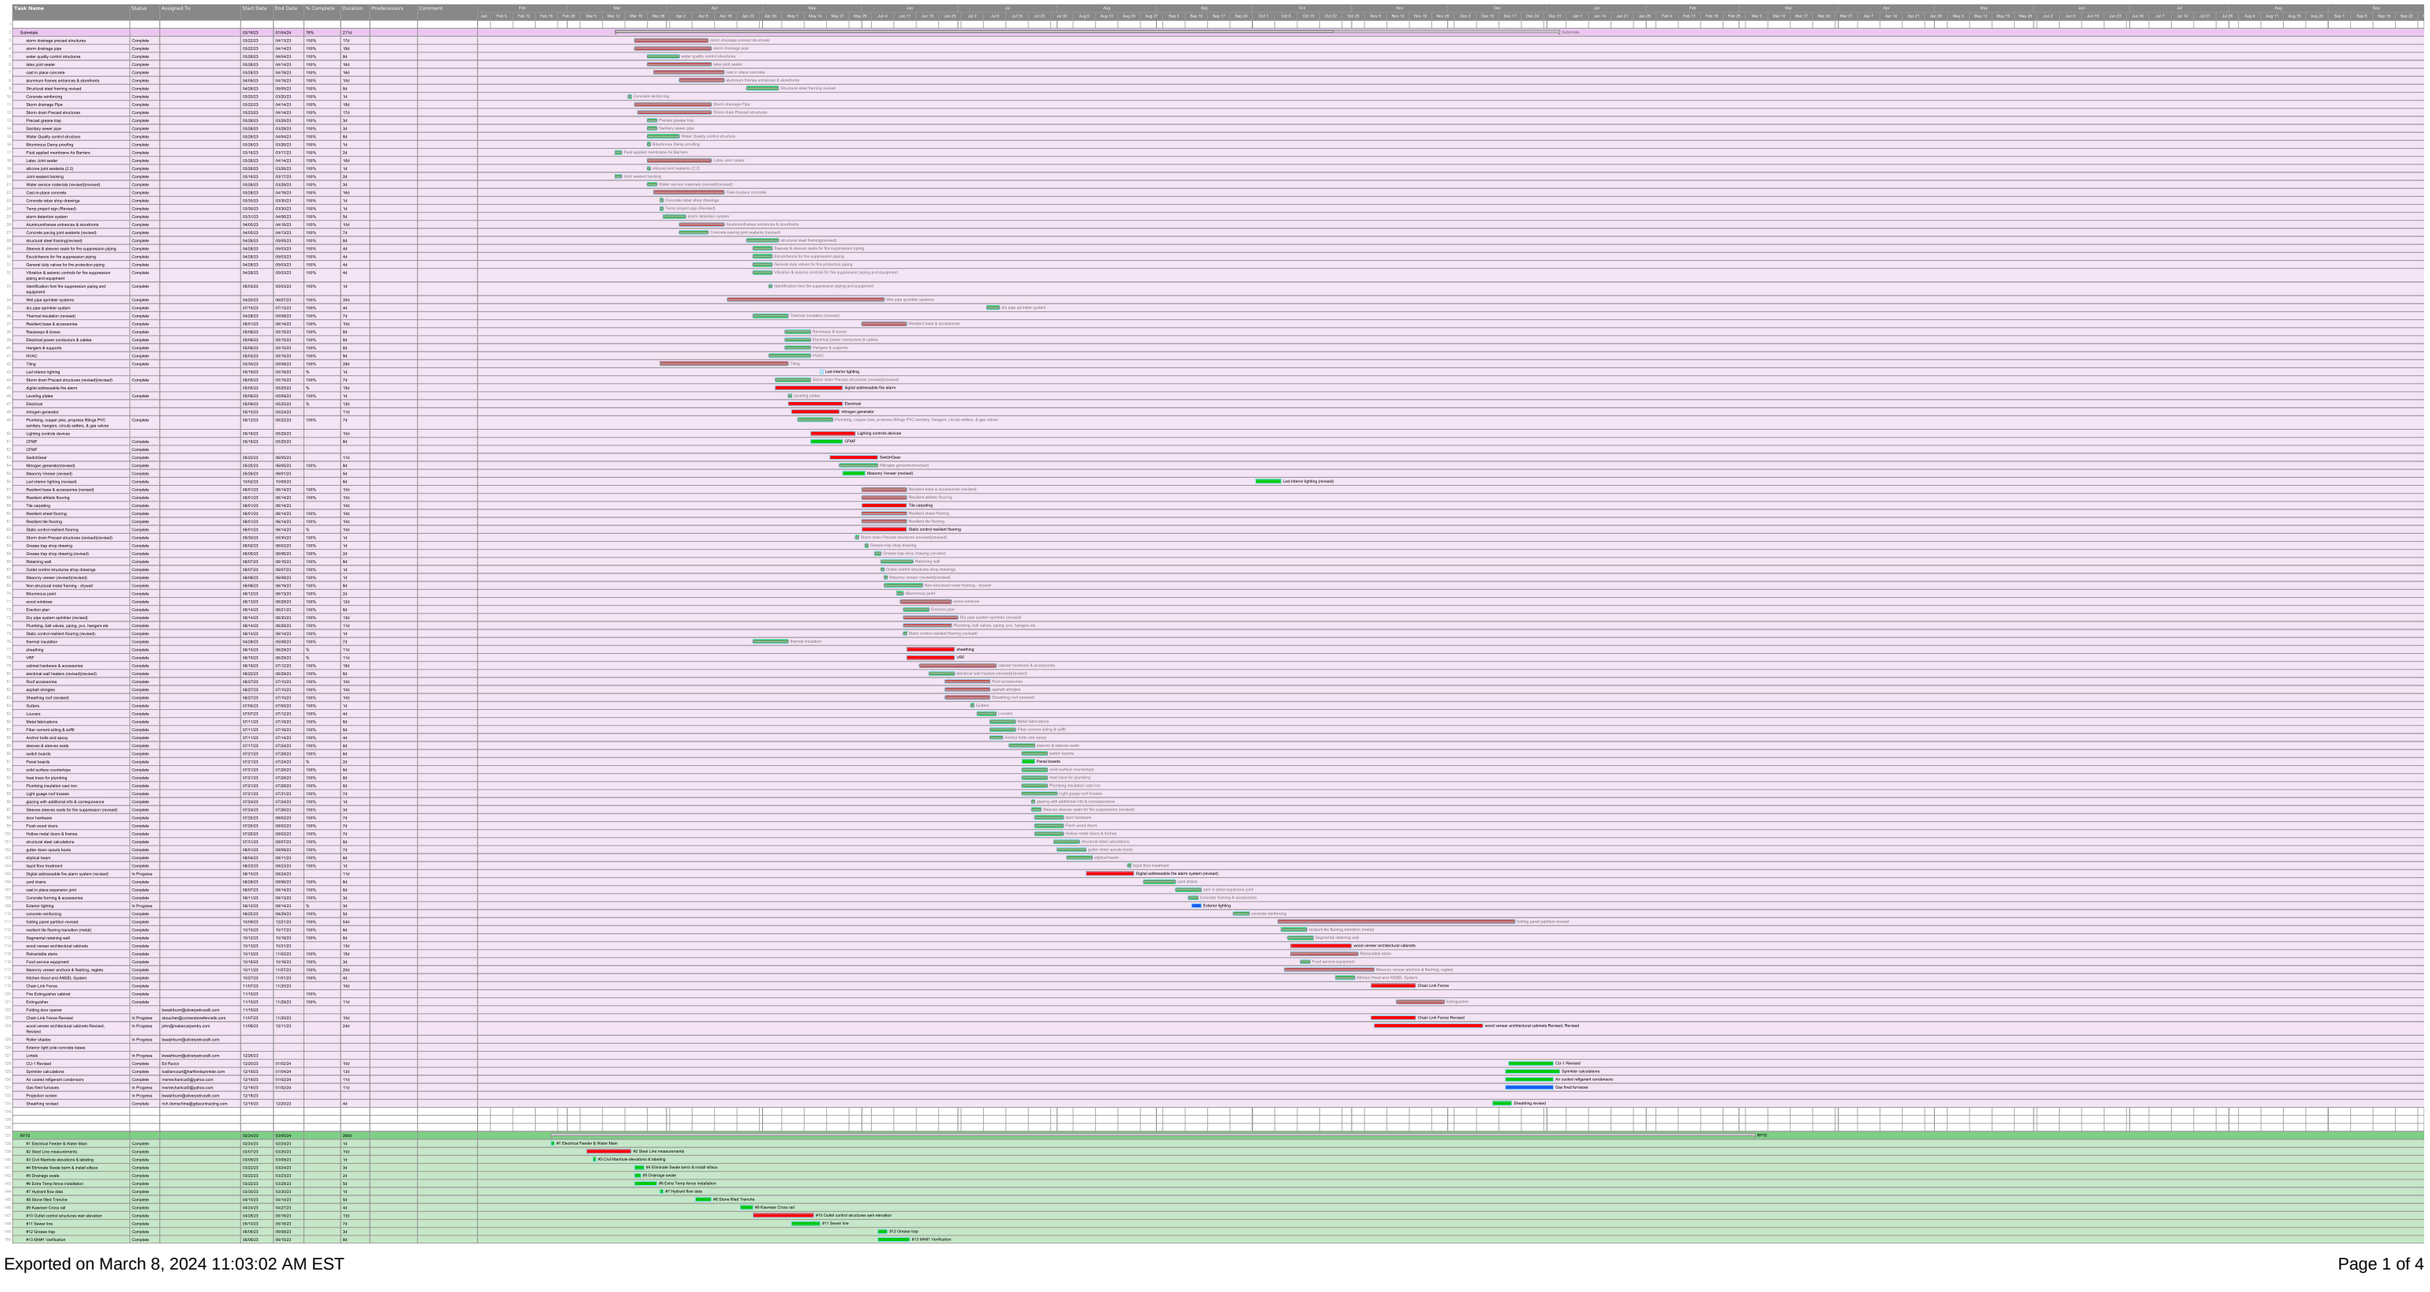

Task Name	Status	Assigned To	Start Date	End Date	% Complete	Duration	Predecessors	Comment
Submittals			03/16/23	01/04/24	78%	211d		
storm drainage precast structures	Complete		03/22/23	04/13/23	100%	17d		
storm drainage pipe	Complete		03/22/23	04/14/23	100%	18d		
water quality control structure	Complete		03/28/23	04/04/23	100%	8d		
latex joint sealer	Complete		03/28/23	04/14/23	100%	16d		
cast in place concrete	Complete		03/28/23	04/14/23	100%	16d		
aluminum frames entrances & storefronts	Complete		04/05/23	04/18/23	100%	10d		
Structural steel framing revised	Complete		04/28/23	05/09/23	100%	8d		
Concrete reinforcing	Complete		03/20/23	03/29/23	100%	7d		
Storm drainage Pipe	Complete		03/22/23	04/14/23	100%	18d		
Storm drain Precast structures	Complete		03/22/23	04/14/23	100%	17d		
Precast grease trap	Complete		03/28/23	03/28/23	100%	3d		
Sanitary sewer pipe	Complete		03/28/23	03/29/23	100%	3d		
Water Quality control structure	Complete		03/28/23	04/04/23	100%	8d		
Bituminous Damp proofing	Complete		03/28/23	03/29/23	100%	1d		
Fluid applied membrane Air Barriers	Complete		03/16/23	03/17/23	100%	2d		
Latex Joint sealer	Complete		03/28/23	04/14/23	100%	16d		
silicone joint sealants (2,2)	Complete		03/28/23	03/28/23	100%	1d		
Joint sealant backing	Complete		03/16/23	03/17/23	100%	2d		
Water service materials (revised)(revised)	Complete		03/28/23	03/29/23	100%	3d		
Cast-in-place concrete	Complete		03/28/23	04/18/23	100%	16d		
Concrete rebar shop drawings	Complete		03/30/23	03/30/23	100%	1d		
Temp project sign (Revised)	Complete		03/30/23	03/30/23	100%	1d		
storm detention system	Complete		03/31/23	04/06/23	100%	5d		
Aluminumframes entrances & storefronts	Complete		04/05/23	04/18/23	100%	10d		
Concrete paving joint sealants (revised)	Complete		04/05/23	04/13/23	100%	7d		
structural steel framing(revised)	Complete		04/28/23	05/05/23	100%	6d		
Sleeves & sleeves seals for fire suppression piping	Complete		04/28/23	05/03/23	100%	4d		
Escutcheons for fire suppression piping	Complete		04/28/23	05/03/23	100%	4d		
General duty valves for fire protection piping	Complete		04/28/23	05/03/23	100%	4d		
Vibration & seismic controls for fire suppression piping and equipment	Complete		04/28/23	05/03/23	100%	4d		
Identification fore fire suppression piping and equipment	Complete			05/03/23	100%	1d		
Wet pipe sprinkler systems	Complete		04/29/23	06/07/23	100%	30d		
dry pipe sprinkler system	Complete		07/19/23	07/13/23	100%	4d		
Thermal insulation (revised)	Complete		04/28/23	05/09/23	100%	7d		
Resilient base & accessories	Complete		08/01/23	05/14/23	100%	15d		
Raceways & boxes	Complete		05/08/23	05/15/23	100%	6d		
Electrical power conductors & cables	Complete		05/08/23	05/15/23	100%	6d		
Hangers & supports	Complete		05/08/23	05/15/23	100%	6d		
HVAC	Complete		05/09/23	05/15/23	100%	5d		
Tiling	Complete		03/30/23	05/08/23	100%	28d		
Led interior lighting			05/19/23	05/19/23	%	1d		
Storm drain Precast structures (revised)(revised)	Complete		05/05/23	05/15/23	100%	7d		
digital addressable fire alarm			05/05/23	05/25/23	%	15d		
Leveling pdeas	Complete		05/08/23	05/09/23	100%	1d		
Electrical			05/08/23	05/25/23	%	13d		
nitrogen generator			05/19/23	05/24/23		11d		
Plumbing, copper pipe, propress fittings PVC sanitary, hangers, circuit setters, & gas valves			05/12/23	05/22/23	100%	7d		
Lighting controls devices			05/19/23	05/29/23		10d		
CPMP	Complete		05/19/23	05/25/23		6d		
CPMP	Complete							
SwitchGear	Complete		05/22/23	06/05/23		11d		
Nitrogen generator(revised)	Complete		05/25/23	06/05/23	100%	8d		
Masonry Veneer (revised)	Complete		06/26/23	06/01/23		5d		
Led interior lighting (revised)			10/02/23	10/09/23		6d		
Resilient base & accessories (revised)	Complete		08/01/23	08/14/23	100%	10d		
Resilient athletic flooring	Complete		08/01/23	08/14/23	100%	10d		
Tile carpeting	Complete		08/01/23	08/14/23		10d		
Resilient sheet flooring	Complete		08/01/23	08/14/23	100%	10d		
Resilient tile flooring	Complete		08/01/23	08/14/23	100%	10d		
Static control resilient flooring	Complete		08/01/23	08/14/23	%	10d		
Storm drain Precast structures (revised)(revised)	Complete		05/19/23	05/30/23	100%	9d		
Grease trap shop drawing (revised)	Complete		06/05/23	06/06/23	100%	2d		
Retaining wall	Complete		06/07/23	06/16/23	100%	8d		
Outlet control structures shop drawings	Complete		06/07/23	06/07/23	100%	1d		
Masonry veneer (revised)(revised)	Complete		06/08/23	06/09/23	100%	2d		
Non-structural metal framing - drywall	Complete		06/08/23	06/19/23	100%	8d		
Bituminous paint			06/12/23	06/13/23	100%	2d		
wood windows	Complete		06/13/23	06/28/23	100%	12d		
Erection plan			06/14/23	06/21/23	100%	6d		
Dry pipe system sprinkler (revised)	Complete		06/14/23	06/26/23	100%	10d		
Plumbing, ball valves, piping, pvc, hangers etc	Complete		06/14/23	06/28/23	100%	11d		
Static control resilient flooring (revised)	Complete		06/14/23	06/14/23	100%	1d		
thermal insulation	Complete		04/28/23	05/09/23	100%	7d		
sheathing	Complete		06/19/23	06/29/23	%	11d		
VRF	Complete		06/19/23	06/29/23	%	11d		
cabinet hardware & accessories	Complete		06/19/23	07/12/23	100%	18d		
electrical wall heaters (revised)(revised)	Complete		06/22/23	06/28/23	100%	5d		
Roof accessories	Complete		06/27/23	07/10/23	100%	10d		
asphalt shingles	Complete		06/27/23	07/10/23	100%	10d		
Sheathing roof (revised)	Complete		06/27/23	07/11/23	100%	10d		
Gutters	Complete		07/06/23	07/06/23	100%	1d		
Louvers	Complete		07/07/23	07/12/23	100%	4d		
Metal fabricators	Complete		07/11/23	07/18/23	100%	6d		
Fiber cement siding & soffit	Complete		07/11/23	07/18/23	100%	6d		
Anchor bolts and epoxy	Complete		07/11/23	07/14/23	100%	4d		
sleeves & sleeves seals	Complete		07/17/23	07/24/23	100%	6d		
swbd boards	Complete		07/21/23	07/28/23	100%	6d		
Panel boards	Complete		07/21/23	07/24/23	%	2d		
solid surface countertops	Complete		07/21/23	07/28/23	100%	6d		
heat trace for plumbing	Complete		07/21/23	07/28/23	100%	6d		
Plumbing insulation cast iron	Complete		07/21/23	07/28/23	100%	6d		
Light guage roof trusses	Complete		07/21/23	07/31/23	100%	7d		
glazing with additional info & correspondence	Complete		07/24/23	07/24/23	100%	1d		
Sleeves sleeves seals for fire suppression (revised)	Complete		07/24/23	07/28/23	100%	3d		
door hardware	Complete		07/25/23	08/02/23	100%	7d		
Flush wood doors	Complete		07/25/23	08/02/23	100%	7d		
Hollow metal doors & frames	Complete		07/25/23	08/02/23	100%	7d		
structural steel calculations	Complete		07/11/23	08/07/23	100%	6d		
gutter down spouts boots	Complete		08/01/23	08/09/23	100%	7d		
elyptical beam	Complete		08/04/23	08/11/23	100%	6d		
liquid floor treatment	Complete		08/23/23	09/23/23	100%	1d		
Digital addressable fire alarm system (revised)	In Progress		08/11/23	08/24/23		11d		
joint drains	Complete		08/28/23	09/06/23	100%	8d		
cast in place expansion joint	Complete		09/07/23	09/14/23	100%	6d		
Concrete forming & accessories	Complete		09/11/23	09/19/23	100%	7d		
Exterior lighting	In Progress		09/14/23	09/14/23	%	3d		
concrete reinforcing	Complete		09/25/23	09/29/23	100%	5d		
folding panel partition revised	Complete		10/09/23	10/21/23	100%	9d		
resilient tile flooring transition (metal)	Complete		10/10/23	10/17/23	100%	6d		
Segmental retaining wall	Complete		10/12/23	10/19/23	100%	6d		
wood veneer architectural cabinets	Complete		10/13/23	10/31/23		13d		
Retractable stairs	Complete		10/13/23	11/02/23	100%	15d		
Food service equipment	Complete		10/16/23	10/18/23	100%	3d		
Masonry veneer anchors & flashing, reglets	Complete		10/17/23	11/07/23	100%	25d		
Kitchen Hood and ANSEL System	Complete		10/27/23	11/01/23	100%	4d		
Chain Link Fence	Complete		11/07/23	11/29/23		15d		
Fire Extinguisher cabinet	Complete		11/16/23		100%			
Extinguisher	Complete		11/15/23	11/29/23	100%	11d		
Folding door opener		tweatburn@silverpetrusatt.com	11/15/23					
Chain Link Fence Revised	In Progress	dbouchie@conversionelectric.com	11/07/23	11/20/23		10d		
wood veneer architectural cabinets Revised, Revised	In Progress	john@blakercarpentry.com	11/08/23	12/11/23		24d		
Roller shades	In Progress	tweatburn@silverpetrusatt.com						
Exterior light pole concrete bases								
Lintels	In Progress	tweatburn@silverpetrusatt.com	12/26/23					
CU-1 Revised	Complete	Ed Pavia	12/20/23	01/02/24		10d		
Sprinkler calculations	Complete	kalliecrouse@fairfieldsprinkler.com	12/19/23	01/04/24		13d		
Air cooled refrigerant condensors	Complete	marie.tkalica@yahoo.com	12/19/23	01/02/24		11d		
Gas fired furnaces	In Progress	marie.tkalica@yahoo.com	12/19/23	01/02/24		11d		
Projection screen	In Progress	tweatburn@silverpetrusatt.com	12/18/23					
Sheathing revised	Complete	rich.donachie@gilbertroofing.com	12/15/23	12/20/23		4d		
BIDS			06/26/23	03/05/24		394d		
#1 Electrical Feeder & Water Main	Complete		12/04/23	02/24/23		1d		
#2 Steel Line measurements	Complete		03/07/23	03/20/23		10d		
#3 Civil Manhole elevations & labeling	Complete		03/08/23	03/09/23		1d		
#4 Eliminate Swale berm & install silleco			03/22/23	03/24/23		3d		
#5 Drainage swale			03/22/23	03/23/23		2d		
#6 Extra Temp fence installation			03/22/23	03/28/23		5d		
#7 Hydrant flow data			03/16/23	03/20/23		1d		
#8 Stone filled Trenche			04/10/23	04/14/23		5d		
#9 Kawneer Cross rail			04/24/23	04/27/23		4d		
#10 Outlet control structures wall elevation			04/28/23	05/16/23		15d		
#11 Sewer line			05/10/23	05/18/23		7d		
#12 Grease trap			06/06/23	06/08/23		3d		
#13 MMP1 Verification			06/06/23	06/15/23		8d		

	Task Name	Status	Assigned To	Start Date	End Date	% Complete	Duration	Predecessors	Comment
151	#14 Ground water concerns	Complete		06/06/23	06/14/23		7d		
152	#15 Retaining wall & concrete walk grades	Complete		06/07/23	06/23/23		13d		
153	#16 Transformer pad	Complete		06/12/23	06/14/23		3d		
154	#17 Foundation drain	Complete		06/12/23	06/19/23		6d		
155	#18 2.2 Gutters	Complete		06/21/23	06/27/23		5d		
156	#19 22 Utilities between foundation & retaining wall	Complete		06/27/23	07/11/23		11d		
157	#20 P 101 Piping coverage	Complete		06/16/23	07/11/23		8d		
158	#21 A 110 Dimension Discrepancies	Complete		06/16/23	07/11/23		8d		
159	#22 Utilities between foundation & retaining wall	Complete		07/11/23	07/11/23		1d		
160	#23 Utilities between foundation & retaining wall	Complete		07/14/23	07/31/23		12d		
161	#24 fire protection 3/4 west system	Complete		07/17/23	07/18/23		2d		
162	#25 Water coming up in the building after heavy rains	Complete		07/18/23	08/11/23		18d		
163	#26 water main connections	Complete		07/25/23	08/22/23		21d		
164	#27 Link seal for kitchen cast iron drain lines with heat lines	Complete		07/25/23	07/27/23		3d		
165	#28 Cast iron drain boots	Complete		07/25/23	07/28/23		2d		
166	#29 Multipurpose room sinks East & west	Complete		07/26/23	07/27/23		2d		
167	#30 panel boards	Complete		07/26/23	08/16/23		16d		
168	#31 Switch board submittal response	Complete		07/31/23	08/07/23		6d		
169	#32 gravel base over detention system	Complete		08/01/23	08/10/23		6d		
170	#33 Manhole 3 invert	Complete		08/01/23	08/07/23		5d		
171	#34 Manhole #1	Complete		08/04/23	08/07/23		2d		
172	#35 use of roller catches & door locks on cabinets	Complete		08/17/23	08/23/23		5d		
173	#36 Elevations & spot grades of retaining wall & building grades	Complete		08/21/23	08/24/23		4d		
174	#37 Exterior piers & interior columns to low	Complete		08/28/23	09/30/23		2d		
175	#38 Interior shear wall anchor bolts	Complete		08/30/23	09/06/23		6d		
176	#39 Electrical conduit running through thicken slab	Complete		08/06/23	09/07/23		2d		
177	#40 Fire sprinkler question	Complete		09/11/23	10/04/23		18d		
178	#41 isolation Joints	Complete		09/14/23	09/25/23		8d		
179	#42 Attic ladder to roof	Complete		09/18/23	09/25/23		6d		
180	#43 thermal break	Complete		09/27/23	10/19/23		17d		
181	#44 Finish floors & slab (add areas that do not match spec)	Complete		10/04/23	10/20/23		13d		
182	#45 Statement of special inspection	Complete		10/02/23	10/11/23		8d		
183	#46 Unsuitable soils for CCD trench unable to compact	Complete		10/11/23	10/19/23		7d		
184	#47 Crack in foundation wall prior to slab pour	Complete		10/17/23	10/17/23		1d		
185	#48 sewer drain in the way of foundation drains to be installed	Complete		10/20/23	10/30/23		7d		
186	#49 Aluminum flashing for windows	Complete		10/27/23	11/15/23		14d		as-provided
187	#50 shear wall s202 detail02 location & sheathing size	Complete		10/31/23	10/31/23		1d		
188	#51 Cracks in slab	Complete		10/31/23	11/08/23		7d		
189	#52 Equipment pads & retaining wall	In Progress	bwashburn@silverpetrucelli.com	11/01/23	11/16/23		11d		RFI was 50% answered resent for the rest
	#52 Equipment pads & retaining wall Sabini	Complete		11/01/23	11/01/23		1d		
190	#56 Follow up from RFI 52	Complete		11/06/23	11/15/23		8d		BIRD requested more information
	#lnk(R52 equipment pads and retaining wall	Complete		11/22/23					
191	#53 Roof drains shallow coverage	Complete		11/02/23					BIRD requested more information
192	#54 Headers for door openings	Complete		11/02/23	11/13/23		8d		clarification requested by spBa (header schedule)
193	#55 exterior finish grades	In Progress	bwashburn@silverpetrucelli.com	11/07/23	11/15/23		7d		
	#56 exterior finish grades sent Partially answered	Complete		11/07/23	11/15/23		7d		
	Requested remaining answer	Complete		11/07/23					
194	#57 Exterior Walls & trusses	Complete		11/07/23	11/14/23		6d		4x4 bearing & walls align
195	#58 Downspout boots mounting	Complete		11/08/23	11/14/23		5d		RL confirmed with BI of catchwater
196	#59 Porte Cochere roof drains	Complete		11/09/23	11/14/23		4d		
197	#60 Exterior door hardware	In Progress	bwashburn@silverpetrucelli.com	11/10/23					
198	#61 B1881 modification	Complete		11/10/23	11/15/23		4d		
199	#62 truss sitting on I beams			11/10/23	12/05/23		17d		
	RFMG Trusses sitting on (I) beam sent	Complete	bwashburn@silverpetrucelli.com	11/10/23	11/28/23		12d		RFMG Trusses sitting on (I) beam sent
	Request for response Emailed	Complete	Robert Lamarre	11/27/23	11/28/23		2d		Request for response Emailed
	GDS Response to E2 requested moore	Complete	rich.dorrenchine@gibsontrenching.com	11/28/23	11/29/23		2d		GDS Response to E2 requested moore
	BIRD responsed to E2 request for locations as indicated on RFI	Complete	Robert Lamarre	11/29/23	11/29/23		1d		BIRD responsed to E2 request for locations as indicated on RFI
	GDS requests engineer for trusses to send email to Team	Complete	rich.dorrenchine@gibsontrenching.com	11/29/23	11/29/23		1d		GDS requests engineer for trusses to send email to Team
	Waiting on E2 response from GDS engineers	Complete	bwashburn@silverpetrucelli.com	12/01/23	12/05/23		3d		Waiting on E2 response from GDS engineers
200	#63 Demising wall between kitchen & dry storage	Complete	bwashburn@silverpetrucelli.com	11/10/23	12/19/23		23d		#63 Demising wall between kitchen & dry storage
201	#64 Retaining wall clarification	In Progress	bwashburn@silverpetrucelli.com	11/22/23					
202	#65 Exposed moment connection	Complete	bwashburn@silverpetrucelli.com	11/28/23	12/05/23		6d		#65 Exposed moment connection
203	#66 bearing seat bracket	Complete	bwashburn@silverpetrucelli.com	11/30/23	12/05/23		4d		#66 bearing seat bracket
204	#67 ItemADR FS Deduct Alternate	Complete	bwashburn@silverpetrucelli.com	11/30/23	12/11/23		8d		#67 ItemADR FS Deduct Alternate
205	#68 DCS Weir issues regarding	Complete	bwashburn@silverpetrucelli.com	12/04/23	12/06/23		3d		#68 DCS Weir issues regarding
206	#69 - Shear Wall SW-4	Complete	bwashburn@silverpetrucelli.com	12/05/23	12/07/23		3d		#69 - Shear Wall SW-4
207	#70 Two Types of light pole bases	In Progress	bwashburn@silverpetrucelli.com	12/06/23	12/07/23		2d		#70 Two Types of light pole bases
208	#71 Kitchen cold door demension	Complete	bwashburn@silverpetrucelli.com	12/07/23	12/11/23		3d		#71 Kitchen cold door demension
209	#72 Folding door partition & Ceiling Height	Complete	bwashburn@silverpetrucelli.com	12/07/23	12/11/23		3d		#72 Folding door partition & Ceiling Height
210	#73 Fire Hydrant location	Complete	bwashburn@silverpetrucelli.com	12/08/23	12/12/23		3d		#73 Fire Hydrant location
211	#74 Gravity Hoods & fresh air intakes	Complete	bwashburn@silverpetrucelli.com	12/08/23	12/13/23		4d		#74 Gravity Hoods & fresh air intakes
212	#75 Spot grades required at Curbing transitions	In Progress	bwashburn@silverpetrucelli.com	12/11/23					SLR change grades and structure elevations/ SLR to revise
213	#76 Eave Detail	Complete	bwashburn@silverpetrucelli.com	12/14/23	12/19/23		4d		#76 Eave Detail
214	#77 Water entering southeast corner of the site	Complete	bwashburn@silverpetrucelli.com	12/22/23					
215	#78 Radius Needed for frame SF04	Complete	bwashburn@silverpetrucelli.com	12/26/23					
216	#79 Lobby entrance detail meeting ante cochere	Complete	bwashburn@silverpetrucelli.com	12/26/23					
217	#80 Tower Ceiling finish detail	Complete	bwashburn@silverpetrucelli.com	12/28/23					
218	#81 Eyebrow Overhang detail Measurement	Complete	bwashburn@silverpetrucelli.com	01/02/24					
219	#82 Cool#100 Attic access door	Complete	bwashburn@silverpetrucelli.com	01/04/24					
220	#83 Coat hooks installation height	Complete	bwashburn@silverpetrucelli.com	01/05/24	01/11/24		5d		#83 Coat hooks installation height
221	#84 Louver sill height	Complete	bwashburn@silverpetrucelli.com	01/08/24	01/09/24		2d		#84 Louver sill height
222	#85 Equipment Pad detail	On Hold	bwashburn@silverpetrucelli.com	01/11/24	01/19/24		6d		#85 Equipment Pad detail
223	#86 Cross pitch locations greater than 2.5%	Complete	bwashburn@silverpetrucelli.com	01/11/24	01/24/24		11d		#86 Cross pitch locations greater than 2.5%
224	#87 Utility spacing between foundation & retaining wall	Complete	bwashburn@silverpetrucelli.com	01/11/24	01/23/24		9d		#87 Utility spacing between foundation & retaining wall
225	#88 Framing & header detail above SF8	Complete	bwashburn@silverpetrucelli.com	01/11/24	01/24/24		9d		#88 Framing & header detail above SF8
226	#89 Interior soffit widths	Complete	bwashburn@silverpetrucelli.com	01/12/24	01/25/24		9d		#89 Interior soffit widths
227	#90 Transformer area layout	On Hold	bwashburn@silverpetrucelli.com	01/23/24	02/09/24		10d		#90 Transformer area layout
228	#91 Patio arch height	Complete	bwashburn@silverpetrucelli.com	01/31/24	02/07/24		5d		#91 Patio arch height
229	#92 W2 attic window gable measurements	Complete	bwashburn@silverpetrucelli.com	02/02/24	02/05/24		2d		#92 W2 attic window gable measurements
230	#93 Trees town hall parking lot	On Hold	bwashburn@silverpetrucelli.com	02/05/24	02/14/24		8d		#93 Trees town hall parking lot
231	#94 plywood cut outs for overlaps	Complete	bwashburn@silverpetrucelli.com	02/06/24	02/14/24		7d		#94 plywood cut outs for overlaps
232	#95 Shingles detail for rakes valley's and ridges	Complete	bwashburn@silverpetrucelli.com	02/07/24	02/14/24		6d		#95 Shingles detail for rakes valley's and ridges
233	#96 Tree town parking lot R1	On Hold	bwashburn@silverpetrucelli.com	02/08/24	02/15/24		6d		#96 Tree town parking lot R1
234	#97 Fire hydrate relocation issue	Complete	bwashburn@silverpetrucelli.com	02/14/24	02/27/24		9d		#97 Fire hydrate relocation issue
235	#98 Column LP1 bigger than propsed wall	In Progress	bwashburn@silverpetrucelli.com	02/20/24					
236	#99 Type (P) fixture	Complete	bwashburn@silverpetrucelli.com	02/22/24	02/26/24		3d		#99 Type (P) fixture
237	#100 Roof drain & down spout near SF8	Complete	bwashburn@silverpetrucelli.com	02/22/24	02/26/24		3d		#100 Roof drain & down spout near SF8
238	#101 Retaining wall concerns based on proposed utility layouts	In Progress	bwashburn@silverpetrucelli.com	02/23/24					
239	#102 Drywall ceiling heights	In Progress	bwashburn@silverpetrucelli.com	02/28/24	03/05/24		6d		#102 Drywall ceiling heights
240	#103 wall flashing detail at tower & cashiniers	In Progress	bwashburn@silverpetrucelli.com	03/06/24					
241	#104 Support for folding partition	In Progress	bwashburn@silverpetrucelli.com	03/07/24					
242									
243									
244	Change orders/ Construction change directive			12/18/24					
245	Electrical building core upgrades	In Progress	bwashburn@silverpetrucelli.com						
	CBC approved pcc request		jamiacambria@cityofgrandbay.ca/chelsie						
	signatures Required		bwashburn@silverpetrucelli.com						
246	CO#1 Silfence Replacement for erosion control	Complete							$3,403.65
247	CO#2 Removal of stone trench & water diversion								$45,270.52
248	Conduit for future generator		bwashburn@silverpetrucelli.com						$14,346.35
249	Over excavation	In Progress							$76,000.00
	SPA# Rejected over excavation								
250	Water connection in road by water dept OML assistant	In Progress							$3,332.93
	SPA# Rejected Water connection credit								
251	CCD#1 water diversion and stone trench	In Progress							$257,364.45
	SPA# rejected CCD water diversion & stone Trench								
252	CO#3 Elliptical credit & foundation upgrades	Complete							$5,248.28
253	Relocate underground electrical pinnacles & telstara lines Revised to include Eversource Request)	In Progress	bwashburn@silverpetrucelli.com						$28,848.92
254	Gas sleeve Conduit	On Hold	Robert Lamarre						$0.00
255	Additional retaining wall Work revised	In Progress	bwashburn@silverpetrucelli.com	12/19/24					$20,708.96
256	PCO#24 Moment connection modification	In Progress	bwashburn@silverpetrucelli.com						$8,084.71
257									**$342,228.36**
258									
259	**Goldwater Senior Center**	**Complete**		**03/06/23**	**11/09/23**	**39%**	**169d**		
260	**Planning**	**Complete**		03/06/23	05/03/23		41d		Planning
261	Building permit application	Complete		03/06/23	03/30/23		16d		Building permit application
262	Comment	Complete		03/17/23	03/22/23		4d		Comment
263	CB+DH 2023/01246	Complete	vk	03/23/23	03/29/23		5d		CB+DH 2023/01246
264	DOT Permit	Complete	vk	03/06/23	03/24/23		15d	21833	DOT Permit
265	**Site Work**	**Complete**		03/31/23	06/19/23	0.4d	70d		Site Work
266	Site clearing			03/31/23	03/31/23	100%	1d		Site clearing
267	Equipment delivery	Complete		04/04/23	04/04/23	100%	1d		Equipment delivery
268	Tree Cutting	Complete	vk	03/06/23	03/06/23	100%	1d		Tree Cutting
269	Stumping	Complete	vk	03/06/23	03/15/23	100%	6d		Stumping
270	Chipping	Complete	vk	03/14/23	03/20/23	100%	5d	Rain 3/11-3/13/3/14	Chipping
271	Temp Facilities	Complete		03/21/23	03/22/23	100%	2d		Temp Facilities
272	Fence	Complete	Robert Lamarre	03/21/23	03/21/23	100%	1d		Fence
273	Office trailer	Complete	Robert Lamarre	03/22/23	03/22/23	100%	1d		Office trailer
274	Porta pot	Complete	Robert Lamarre	03/23/23	03/23/23	100%	1d		Porta pot
275	Site excavation			03/21/23	05/15/23	92%	37d		Site excavation
276	Geotechnical engineering Requested	Complete		03/21/23	04/06/23	100%	13d	255	Geotechnical engineering Requested
277	Stripping top soil & Stockpiling	Complete	vk	03/22/23	05/15/23	100%	35d	276FS -1V	Stripping top soil & Stockpiling
278	Cutting & fill to grade	Complete	vk	03/22/23	05/09/23	85%	35d	276FS -1V	Cutting & fill to grade
279	Erosion control	Complete		03/22/23	03/31/23	100%	8d		Erosion control
280	Infill	Complete	bwashburn@silverpetrucelli.com	03/22/23	03/28/23	100%	5d		Infill
281	Silt Sox	Complete		03/27/23	03/31/23	100%	5d	256	Silt Sox
282	Track pad	Complete		03/06/23	03/30/23	100%	1d		Track pad
283	Hydrants	Complete		03/31/23	03/31/23	100%	1d		Hydrants
284	Excessive water concerns BRD requested SLR site visit	Complete	bwashburn@silverpetrucelli.com	04/28/23	05/01/23	0%	3d		Excessive water concerns BRD requested SLR site visit
285	RFMG Stone Filled Trenches	Complete	bwashburn@silverpetrucelli.com	04/19/23	04/19/23	100%	1d		RFMG Stone Filled Trenches
286	DTE report1	Complete	bwashburn@silverpetrucelli.com	04/07/23	04/10/23	100%	2d	291	DTE report1
287	Requested PCO#9 stone trench	Complete	bwashburn@silverpetrucelli.com	04/19/23	04/20/23	100%	2d		Requested PCO#9 stone trench
288	SPA# review PCO#9	Complete	bwashburn@silverpetrucelli.com	04/21/23	04/24/23	100%	2d	302	SPA# review PCO#9
289	BRD revised PCO#9	Complete	Robert Lamarre	04/25/23	04/25/23	100%	1d	303	BRD revised PCO#9
290	OML completed stone trench	Complete	vk	04/21/23	05/15/23	99%	19d	302	OML completed stone trench
291	Excavability for Building	Complete	vk	05/16/23	05/16/23	100%	1d	339	Excavability for Building
292	Northeast wall Building	Complete	vk	05/16/23	05/16/23	100%	1d	293	Northeast wall Building
293	South Wall of Building	Complete	vk	05/16/23	05/16/23	100%	1d	307	South Wall of Building
294	Northwest Wall building	Complete	vk	05/17/23	05/19/23	100%	3d	308	Northwest Wall building
295	North wall of building	Complete	vk	05/22/23	05/25/23	100%	4d	309	North wall of building
296	Concrete Building			05/22/23	06/14/23	99%	19d		Concrete Building
297	Footings			05/22/23	06/02/23	100%	10d		Footings
298	forming	Complete	akonorenkets@gmail.com	05/22/23	05/31/23	100%	8d	308	forming
299	Rebar	Complete	akonorenkets@gmail.com	05/22/23	05/31/23	100%	8d	21355	Rebar
300	Inspection			05/23/23	05/23/23	100%	1d	21355	Inspection
301	Pour	Complete	akonorenkets@gmail.com	06/02/23	06/02/23	100%	1d	21355	Pour
302	Foundation Walls	Complete		05/25/23	06/14/23	99%	15d		Foundation Walls
303	forming	Complete	akonorenkets@gmail.com	05/25/23	06/14/23	100%	15d	21355 +5d	forming
304	Rebar	Complete	akonorenkets@gmail.com	05/25/23	06/13/23	100%	14d	21355	Rebar
305	Inspection	Complete		05/25/23	05/25/23		1d	21355	Inspection

	Task Name	Status	Assigned To	Start Date	End Date	% Complete	Duration	Predecessors	Comment
312	Pour	Complete	aboerendelis@gmail.com	05/25/23	06/14/23	100%	15d	3185	
313	Completed foundation walls			06/14/23	06/14/23		0	321	
314	Dampproofing	Complete		06/14/23	06/16/23	100%	3d		
315	Foundation walls	Complete	cfuree@dmytuvn.com	06/14/23	06/14/23	100%	1d	321FS -1d	
316	Styrofoam Mat drain	Complete	cfuree@dmytuvn.com	06/14/23	06/16/23	100%	3d	324SS	
317	**Backfilling building**	**Complete**		06/12/23	07/05/23	17%	16d		
318	REF#17 Footing Drain connection	Complete	bwashburn@silverpetrucelli.com	06/12/23	06/16/23	100%	4d	322FS -3d	
319	Backfilling inside & outside of the building	Complete	cfr	06/13/23	07/05/23	75%	15d	324FS -2d	
320	Footing Drains	Canceled	cfr	06/16/23	06/19/23	0%	2d	322FS -2d	Omitted from project By design team
321	**Underground Utilities**	**Complete**		07/06/23	11/09/23	3.8%	83d		
322	Plumbing	Complete		07/06/23	08/14/23	100%	28d	324FS +1d	
323	PVC Drain lines	Complete	Ed Rueca	07/06/23	07/06/23	100%	1d		
324	Partial Inspection			07/07/23	07/07/23	100%	1d	322	
325	Relayed stuff over iron	Complete	Ed Rueca	07/14/23	07/14/23	100%	1d	323	
326	RFI#25 Water & air coming up from slab	Complete	bwashburn@silverpetrucelli.com	07/17/23	08/11/23	100%	20d	324SS +1d	
327	Cast Iron	Complete	Ed Rueca	07/20/23	07/31/23	100%	7d	324FS +4d	Plan 4 day
328	Inspection Cast iron			07/31/23	07/31/23	100%	1d	326FF	
329	Heat Trace Lines	Complete	Ed Rueca	08/01/23	08/01/23	100%	1d	327	
330	Cast iron insulation	Complete	jeff@overall-steel.com	08/02/23	08/10/23	100%	7d	328	
331	Cast iron Insulation inspection	Complete		08/11/23	08/11/23	100%	1d	329FF	
332	Electric	Complete		07/06/23	11/09/23	9%	91d		
333	Pre Conduit & boxes	Complete	ESG	09/07/23	09/11/23	100%	3d	307FS -3d	
334	Inspection	Complete	ESG	09/07/23	09/07/23	100%	1d	3435S	
335	Re-Install 2"&3" conduit in stone	Complete	Robert Lamons	09/08/23	09/08/23	100%	1d	307FF -1d	
336	**Drainage System**	**Complete**		07/06/23	11/09/23	3.8%	83d		
337	Sewer Line	Complete	cfr	07/11/23	07/17/23	100%	5d	334FS -4d	
338	Grease trap	Complete	cfr	07/18/23	07/18/23	90%	1d	348	
339	Catch basin #19.9	Complete	cfr	07/19/23	07/19/23	90%	1d	347	
340	Catch basin #9.7	Complete	cfr	07/20/23	07/20/23	90%	1d	348	
341	Catch basin #0.5	Complete	cfr	07/21/23	07/21/23	90%	1d	349	
342	Catch Basin #4	Complete	cfr	11/08/23	11/08/23	90%	1d	374, 373	
343	MH-1	Complete	cfr	08/30/23	08/31/23	90%	2d	371	
344	MH-2	Complete	cfr	07/21/23	07/21/23	90%	1d	349	
345	MH-3	Complete	cfr	07/24/23	07/24/23	90%	1d	346	
346	Detention System	Complete	cfr	11/09/23	11/09/23	100%	1d	351, 376	
347	Roof Drains	On Hold	cfr			0%		Plumbing RFI	
348	**Site Underground Utilities**	**Complete**		07/06/23	08/03/23	3.8%	20d		
349	Installation of water & Fire lines Stub up into building	Complete	cfr	07/06/23	07/12/23	99%	5d	332SS +1d	
350	Domestic Waterline RFI#26	Complete	bwashburn@silverpetrucelli.com	07/26/23	08/01/23	100%	5d	334FS +6d	
351	PCO#16 Water connection in the road	Complete	Robert Lamons	08/02/23	08/08/23	0%	5d	334FS +6d	
352	TOCWD	Complete	santaroselunds@grupomvilleu@scholeland.go	08/06/23	08/23/23	100%	11d	365	
353	Water &Fire shred connection	Complete	santaroselunds@grupomvilleu@scholeland.go	08/22/23	09/22/23	100%	5	361FS -1d	
354									
355									
356	**Slab Prep**	**Complete**		07/17/23	09/11/23	1	41d	334	
357	Installation of Vaporbars	Complete	cfr	07/17/23	09/11/23	100%	41d	332SS +2d, 33K	
358	Installation of Mono	Complete	cfr	07/17/23	09/11/23	100%	41d	332	
359	PCO # 19 Water diversion	Complete	bwashburn@silverpetrucelli.com	08/14/23	08/16/23	100%	3d	339	
360	PCO#20 Footing drains added back to project	Complete	bwashburn@silverpetrucelli.com	08/14/23	08/16/23	100%	3d	363SS	
361	Construction change directive (CCD)	Complete		08/28/23	11/07/23	90%	52d		
362	Construction change directive	Complete	bwashburn@silverpetrucelli.com	08/28/23	09/28/23	100%	1d	338FS +10d, 362	
363	CCD Signed by town	Complete	bwashburn@silverpetrucelli.com	08/28/23	08/28/23	100%	1d	371SS	
364	Footing Drains Added back to scope	Complete	bwashburn@silverpetrucelli.com	08/28/23	11/07/23	100%	52d	372SS	
365	Transit pipe connection	Complete	cfr	08/28/23	11/07/23	100%	52d	372SS	
366	RFI#46 Unavailable soils for (CCD)	Complete	erin.bass@evensource.com	11/02/23	11/02/23	24%	1d	315FS -10d	
367	**Structural steel**	**Complete**		09/25/23	09/25/23	1.67	31d		
368	Structural steel delivery & installation	Complete	jeff@overall-steel.com	08/25/23	09/25/23	100%	1d	314SS +1d	
369	RFI#21 Exterior piers & columns poured to low	Complete	bwashburn@silverpetrucelli.com	08/25/23	08/30/23	100%	2d	377SS	
370	Demo existing piers	Complete	cfr	08/31/23	08/31/23	100%	1d	378	
371	Re-grouted 11 columns	Complete	aboerendelis@gmail.com	08/31/23	08/31/23	100%	1d	379SS	
372	Form & pour exterior piers	Complete	aboerendelis@gmail.com	09/01/23	09/21/23	100%	15d	369	
373	Re-set columns	Complete	jeff@overall-steel.com	09/22/23	09/22/23	100%	1d	381	
374	Install beams	Complete	jeff@overall-steel.com	09/25/23	09/27/23	100%	3d	383P	
375	Welding	Complete	jeff@overall-steel.com	09/27/23	09/27/23	100%	1d	383FF	
376	Steel inspection	Complete		09/22/23	09/22/23	100%	1d	384	
377	UT inspection	Complete		09/26/23	09/26/23	13%	1d	383FS +1d	
378	**Concrete slab**	**Complete**		09/01/23	10/09/23	3.89	25d		
379	Slab composition Approved by SP&A to pour	Complete	bwashburn@silverpetrucelli.com	09/01/23	09/01/23	100%	1d	334FS +16d	
380	Vapor barrier	Complete	aboerendelis@gmail.com	09/04/23	09/05/23	100%	2d	368	
381	Rebar	Complete	aboerendelis@gmail.com	09/06/23	09/07/23	100%	2d	369	
382	E2 Unacheduls inspection BRO not notified	Complete		09/18/23	09/19/23	100%	1d	364FS +5d	
383	Wire mesh	Complete	aboerendelis@gmail.com	09/19/23	09/22/23	100%	4d	301	
384	Slab prep inspect rebar wire mesh INITL			09/22/23	09/22/23	100%	1d	382FF	
385	Re-inspection E2	Complete		10/13/23	10/13/23	100%	1d	382FS +16d	
386	Correction to slab prep	Complete	rebar@nhareassociates.com	10/16/23	10/18/23	100%	3d	384	
387	E2 approved correction	Complete	aboerendelis@gmail.com	10/19/23	10/24/23	100%	4d	386	
388	Slab poured	Complete	aboerendelis@gmail.com	10/26/23	10/26/23	90%	1	384FS +2d	
389	Concrete piers (carpet)	Complete		10/16/23	10/17/23	100%	2d		
390	excavation	Complete	cfr	10/10/23	10/10/23	100%	1d	334FS -4d	
391	form &rebar	Complete	aboerendelis@gmail.com	10/11/23	10/12/23	100%	2d	389	
392	Form & rebar inspection	Complete	aboerendelis@gmail.com	10/12/23	10/13/23	100%	1d	406	
393	Pouring piers	Complete	aboerendelis@gmail.com	10/13/23	10/13/23	100%	1d	401SS	
394	Mortrivues paint	Complete	cfuree@dmytuvn.com	10/16/23	10/16/23	100%	1d	402	
395	backfill	Complete	cfr	10/17/23	10/17/23	100%	1d	403	
396	**CFMF**	**In Progress**		10/18/23	11/14/23	3.75	18d		
397	Layout	In Progress	rich.stanschina@tpiconstruction.com	11/08/23	11/13/23	89%	3d	318FS -1d	
398	CFMF Material delivery	In Progress	rich.stanschina@tpiconstruction.com	11/14/23	11/14/23	60%	1d	416	
399	Framing Structural walls			11/15/23	12/07/23	85%	17d		
400	Left side of the building	In Progress	rich.stanschina@tpiconstruction.com	11/15/23	11/22/23	100%	5d	407	
401	Inspection (partial)	In Progress	rich.stanschina@tpiconstruction.com	11/23/23	11/23/23	100%	1d	408	
402	Middle of the building	In Progress	rich.stanschina@tpiconstruction.com	11/28/23	12/04/23	100%	5d	408FS +5d	
403	Inspection (partial)	Complete		12/05/23	12/05/23	100%	1d	411	
404	Right side of the building	In Progress	rich.stanschina@tpiconstruction.com	12/06/23	12/07/23	20%	5d	411	
405	Inspection (partial)			12/07/23	12/07/23	0	0	412	
406	Truss Installation			12/08/23	12/07/24	72%	91d		
407	Left side of the building	In Progress	rich.stanschina@tpiconstruction.com	12/08/23	12/28/23	100%	15d	413	Rain 12/11 &12/12 2 days added
408	Weather delay			12/28/23	12/29/23		2d	413FS -1d	
409	Inspection (partial)			01/01/24	01/01/24	100%	1d	417	
410	Middle of the building	In Progress	rich.stanschina@tpiconstruction.com	01/02/24	01/29/24	100%	15d	418, 421	
411	weather delays			01/29/24	02/09/24		8d	421FS -1d	
412	Inspection (partial)	Not Started		02/09/24	02/09/24	100%	1d	425	
413	Right side of the building		rich.stanschina@tpiconstruction.com	02/09/24	03/06/24	85%	19d	425	
414	Weather delay			02/26/24	03/06/24		8d	422FS -8d	
415	Inspection (partial)			03/07/24	03/07/24		1d	422	
416	Roof sheathing	In Progress		01/01/24	03/12/24	42%	52d		
417	Left side of the building	In Progress	rich.stanschina@tpiconstruction.com	01/01/24	01/03/24	100%	3d	417, 418SS	
418	Phoenix Delivery	In Progress		01/02/24	01/08/24		5d	424FS -2d	shipping delay 5 days
419	Middle of the building		rich.stanschina@tpiconstruction.com	01/08/24	02/02/24	100%	6d	419, 426	
420	weather delays (extreme cold)			01/26/24	02/09/24		8d	424FS -4d	
421	Right side of the building		rich.stanschina@tpiconstruction.com	02/07/24	03/12/24	75%	4d	420, 426	
422	Wall sheathing	In Progress		01/04/24	01/23/24	90%	14d		
423	East side	In Progress	rich.stanschina@tpiconstruction.com	01/04/24	01/17/24	90%	10d	428	
424	West side	In Progress	rich.stanschina@tpiconstruction.com	01/23/24	01/23/24	90%	1	412FS +6d	
425	Pebble metal Frames	Not Started		01/31/24	02/16/24	38%	12d		
426	Interior Installation Door Frames		rich.stanschina@tpiconstruction.com	01/31/24	02/09/24	100%	5d	412FS +5d	
427	Interior Blocking		rich.stanschina@tpiconstruction.com	02/07/24	02/09/24		3d	426	
428	Soffit framing		rich.stanschina@tpiconstruction.com	02/12/24	02/16/24		4d	418	
429	**Thermals**	**Not Started**		02/26/24	03/15/24	17.14	15d		
430	Roofing	Not Started		03/13/24	03/28/24		12d		
431	Right side of the building		michael@planroffing.com	03/13/24	03/19/24		5d	439	
432	Middle of the building		michael@planroffing.com	03/20/24	03/25/24		5d	440	
433	Left side of the building		michael@planroffing.com	03/26/24	04/04/24		5d	441	
434	Fluid applied membrane	Not Started		01/24/24	03/06/24	20%	31d		
435	Fluid applied membrane Walls		cluxes@dmytuvn.com	01/24/24	03/06/24	10%	31d	433	
436	EIFS in screwig walls			02/04/24	03/05/24	100%	5d	434FS -5d	
437	Weather delay			02/25/24	03/05/24	100%	11d	418FS -11d	
438	Aluminum storefronts	Not Started		03/17/24	03/20/24		4d		
439	Left side of the building		anthony@crazydesco.com	03/17/24	03/19/24		3d	443SS -2d	
440	Middle of the building		anthony@crazydesco.com	03/18/24	03/20/24		3d	448	
441	Right side of the building		anthony@crazydesco.com	03/25/24	03/25/24		1	449	
442	Masonry	Not Started		03/06/24	04/16/24		31d		
443	Left side of the building		lobeiter@webster.com	03/06/24	03/19/24		10d	426	429
444	Middle of the building		lobeiter@webster.com	03/20/24	04/02/24		10d	452	
445	Right side of the building		lobeiter@webster.com	04/03/24	04/16/24		10d	453	
446	Cementeus Siding	Not Started		04/03/24	05/14/24		30d		
447	East side		michael@planroffing.com	04/03/24	04/23/24		15d	453	
448	West side		michael@planroffing.com	04/24/24	05/14/24		15d	454	
449	**MEP's Rough-in**	**Not Started**		03/27/24	06/07/24		50d		
450	Hvac	Not Started		03/27/24	04/25/24		20d		
451	Equipment		Ed Rueca	03/27/24	03/27/24		1d	456	
452	Ducts		mansumar1ali2@yahoo.com	03/28/24	04/24/24		20d	455	
453	Inspection			04/25/24	04/25/24		1d	461	
454	Sprinkler system	Not Started		03/28/24	04/30/24		24d		
455	Left side of the building		kaitlancrouff@wrtfirstplumbin.com	03/28/24	04/10/24		10d	461SS	
456	Middle of the building		kaitlancrouff@wrtfirstplumbin.com	04/08/24	04/19/24		10d	458FS -3d	
457	Right side of the building		kaitlancrouff@wrtfirstplumbin.com	04/17/24	04/30/24		10d	458FS -3d	
458	Inspection			04/30/24	04/30/24		0	456	
459	Plumbing	Not Started		03/27/24	04/19/24		21d		
460	Equipment		Ed Rueca	03/27/24	03/27/24		1d	463SS	
461	Waterline		Ed Rueca	03/27/24	04/03/24		10d	463SS	
462	PVC stainless		Ed Rueca	04/04/24	04/17/24		10d	470	
463	Inspection			04/18/24	04/18/24		1d	471	
464	Electrical	Not Started		04/10/24	05/31/24		35d		
465	Branch circuits		ESG	04/10/24	04/22/24		9d	464FS -1d	
466	In-Wall roughs		ESG	04/22/24	05/09/24		14d	474FS -1d	
467	COMI Electrical Building code upgrade		ESG	04/23/24	04/24/24		2d	473SS +1d	
468	Overhead mechanical feeders		ESG	05/07/24	05/17/24		9d	473FS -2d	
469	Power distribution feeders		ESG	05/16/24	05/30/24		11d	477FS -2d	
470	Inspection			05/31/24	05/31/24		1d	478	
471	**Finishes**	**Not Started**		05/17/24	08/19/24		61d		
472	Drywall	Not Started		05/17/24	06/20/24		25d		
473	Drywall installation		rich.stanschina@tpiconstruction.com	05/17/24	06/13/24		15d	474SS	
474	Taping/compound (LS)		rich.stanschina@tpiconstruction.com	06/07/24	06/20/24		10d	482FS -5d	
475	Interior Door slab Installation Hardware	Not Started	Robert Lamons	05/18/24	06/25/24		5d	483FS -3d	
476	Wall covering &protection	Not Started		06/21/24	07/12/24		16d		
477	Wall covering		office@quempercleglio.com	06/21/24	06/25/24		3d	469	
478	FRP		rich.stanschina@tpiconstruction.com	06/26/24	06/28/24		3d	488	
479	Painting		office@quempercleglio.com	07/01/24	07/12/24		10d	497	
480	Folding Partition Door	Not Started		06/21/24	07/01/24		7d		
481	Track & motor installation			06/21/24	06/24/24		2d	484FS -2d	
482	Panel installation			06/25/24	07/01/24		5d	486	
483	Acoustical	Not Started		06/21/24	07/16/24		20d		
484	Acoustical grid			06/21/24	07/04/24		10d	469	
485	Acoustical Tile			07/05/24	07/16/24		10d	503FS -5d	
486	Above ceiling inspection			07/08/24	07/09/24		1d	494SS	
487	Casework	Not Started		07/12/24	08/01/24		15d		
488	Interior trim		john@mallorcarpentry.com	07/12/24	07/19/24		5d	493SS, 494FS -5d	
489	Alternate#5 Wainscot panels & stiles		john@mallorcarpentry.com	07/17/24	07/24/24		6d	487FS -2d	
490	Alternate#6 Coffered Ceiling		john@mallorcarpentry.com	07/17/24	07/26/24		10d	494SS	
491	Cabinets		john@mallorcarpentry.com	07/19/24	08/01/24		10d	494SS +2d	
492	Flooring	Not Started		07/23/24	08/19/24		19d		
493	Left side of the building		kyle@fleetfloors.com	07/23/24	07/30/24		6d	493SS +2d	
494	Middle of the building		kyle@fleetfloors.com	07/31/24	08/07/24		6d	512	
495	Right side of the building		kyle@fleetfloors.com	08/15/24	08/19/24		3	513FS +5d	
496	Appliances	Not Started		08/05/24	08/14/24		8d		
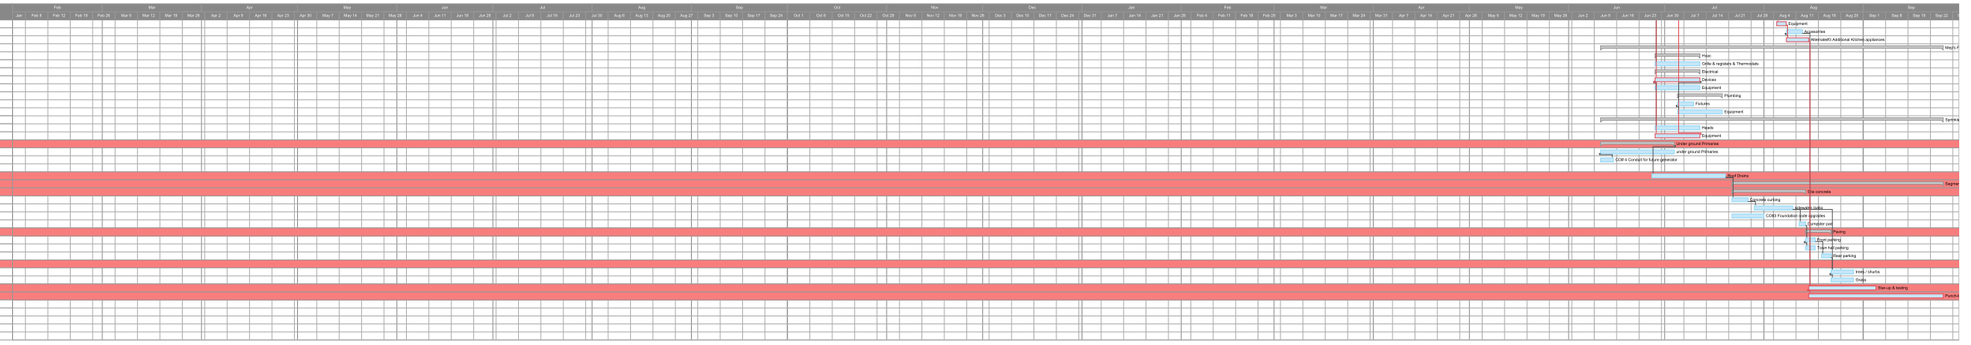
	Task Name	Status	Assigned To	Start Date	End Date	% Complete	Duration	Predecessors	Comment
859	Equipment			08/06/24	09/07/24		3d	913PS -5d	
860	Accessories			08/08/24	09/12/24		3d	914	
861	Alternate#3 Additional Kitchen appliances			08/08/24	09/14/24		5d	914, 917SS	
862	Mack Finishes	Not Started		08/11/24	09/25/24		77d		
863	Hvac			08/28/24	07/11/24		10d		
864	Grills & registers & Thermostats		reviewhardrock@yahoo.com	08/28/24	07/11/24		10d	859FS -5d	
865	Electrical	Not Started		08/28/24	07/11/24		10d		
866	Devices		ESG	08/28/24	07/11/24		10d	859FS -5d	
867	Equipment		ESG	08/28/24	07/11/24		10d	913SS	
868	Plumbing	Not Started		07/05/24	07/18/24		10d		
869	Fixtures		Ed Kusco	07/05/24	07/19/24		3d	913FS -5d	
870	Equipment		Ed Kusco	07/05/24	07/18/24		10d	914SS	
871	Sprinkler	Not Started		08/11/24	09/25/24		77d		
872	Heads		nathanscott@hartlineplumbin.com	08/28/24	07/11/24		10d	913SS	
873	Equipment		nathanscott@hartlineplumbin.com	08/28/24	07/11/24		10d	913SS	
874	**Under ground Primaries**	**Not Started**	**ESG**	08/11/24	07/03/24		77d		
875	under ground Primaries		ESG	08/11/24	07/03/24		77d		
876	COM 4 Conrad for future generator		ESG	08/11/24	09/14/24		4d	920SF +4d	
877									
878	**Roof Drains**	**Not Started**	**vik**	06/07/24	07/19/24		27d	**920FS -5d**	
879	**Segmental wall**	**Not Started**	**vik**	07/22/24	08/30/24		25d	**928**	
880	**Site concrete**	**Not Started**		07/22/24	08/15/24		17d		
881	Concrete curbing		carsen@excelcrete.com	07/22/24	07/29/24		5d	925	
882	sidewalks (walk)		carsen@excelcrete.com	07/29/24	08/09/24		11d	928	
883	COM1 Foundation (only upgrades		carsen@excelcrete.com	07/22/24	07/31/24		8d	924ss2	
884	Dumpster pad		carsen@excelcrete.com	08/12/24	08/13/24		2d	928	
885	**Paving**	**Not Started**		08/14/24	08/27/24		9d		
886	Front parking		vik	08/14/24	08/16/24		3d	911	
887	Town hall parking		vik	08/14/24	08/16/24		3d	933SS	
888	Rear parking		vik	08/19/24	08/21/24		3d	933	
889	**Planting**	**Not Started**		08/22/24	09/06/24		12d		
890	trees / shurbs			08/22/24	08/26/24		5d	926, 928	
891	Grass			08/22/24	08/26/24		5d	927SS	
892	**Start-up & testing**	**Not Started**	**Robert Lanuera**	09/16/24	09/30/24		10d	**920FS -20, 30d**	
893	**Punchlist final inspection**	**Not Started**	**Robert Lanuera**	09/16/24	09/30/24		31d	**939SS**	
894									
895									
896									
897									
898
